Shelf Voice: 09 Implementation and Release Plan

Oct 27, 2026 · @Aradhya Chaudhary

Draft v0.2. All six planning decisions recorded; waiting for the owner's approval.

This plan turns documents 01 to 08 into dated work. Build runs Oct 27 to the Nov 4 noon IST freeze, and all Must requirements have to pass by Nov 1.

Decisions

#	Decision	Options (recommendation %)	Why the top option	Owner's choice
I1	Team split	By layer: frontend, backend and data, AI and quality (60%); by feature, each person owns whole features end to end (40%)	One owner each for UI consistency, RLS and prompts; every feature crosses all three layers anyway	By layer
I2	Build order	Thin slice first: voice setup to live storefront by Oct 30 (70%); layer by layer, full schema and API before any UI (30%)	Proves the riskiest path (mic, transcription, Muse Spark, confirm) early and gives a demoable product by day 4	Thin slice first
I3	If Musts are not all passing on Nov 1	Nov 2 goes to fixing Musts; FR-10 starts only once they pass (70%); start FR-10 in parallel anyway (30%)	A broken Must costs more score than a missing Should	Fix Musts first
I4	Real-owner validation	3 shop owners try it Nov 2 to 3, with signed consent and quotes for the video (65%); 1 owner (25%); none, demo shop only (10%)	Impact is 30% of the score, and the PRD target is 3 real owners	3 owners

#	Decision	Options (recommendation %)	Why the top option	Owner's choice
I5	Internal submit target	Submit by Nov 4, 11 PM IST, 8.5 hours before the deadline (70%); submit just before Nov 5, 7:30 AM IST (30%)	Leaves time to retry a failed upload or form	Nov 4, 11 PM IST
I6	Task tracking	GitHub Issues with a Projects board, one issue per task, linked to PRs (55%); this doc's table only (30%); an Asana project (15%)	Lives next to the code; status moves when PRs merge; this doc stays the summary	GitHub Issues + Projects

Goal and deadline

The goal is a public, working Shelf Voice where every Must requirement passes, submitted with a 2 to 3 minute demo video before Nov 5, 7:30 AM IST. US clocks move back on Nov 1, so the organiser's ET times below are EST (UTC minus 5).

Moment	Organiser time (ET)	Team time (IST)
Code freeze (R4)	Wed Nov 4, 1:30 AM	Wed Nov 4, 12:00 PM
Internal submit target (I5)	Wed Nov 4, 12:30 PM	Wed Nov 4, 11:00 PM
Submission deadline	Wed Nov 4, 9:00 PM	Thu Nov 5, 7:30 AM
Last moment to claim API credits	Wed Nov 4, 9:00 PM	Thu Nov 5, 7:30 AM
Judging	Nov 5 to 8	Nov 5 to 8
Closing ceremony, top 10 live final	Mon Nov 9, 12:00 PM	Mon Nov 9, 10:30 PM

From Oct 27, 5 PM IST to the freeze is about 7 days and 19 hours. Credits are claimed on day 1, not near the deadline.

The submission is done when:

- Every Must passes on production against the document 04 acceptance checks: FR-01 to FR-09, FR-11 and FR-16.
- "Try the demo shop" works with no sign-in, on a seeded shop with 90 days of sales.

- The release checklist in document 08 is all PASS or NOT APPLICABLE on the submitted commit.
- The repo is public, with a README covering setup, architecture and the Meta models used.
- The demo video is recorded from that exact release.
- Meta API spend is under $100 of the $150 credit.

Team and rhythm

The three teammates each own one layer (I1), and each reviews one other's PRs, so no area depends on a single person.


Role	Owns	Reviews	Backup for
A: Frontend and design	App shell, mic capture and WAV, confirm screens, storefront, review page, PWA, accessibility, demo video	C's prompts as they show on screen	Release checklist
B: Backend and data	Supabase schema, RLS, auth, storage, forecast, CI/CD, deploys, backups, seeded demo shop	A's PRs	Meta API client
C: AI and quality	Meta API client, prompts, transcription, evals, observability, spend caps, security checks	B's PRs	Storefront

Open question: which teammate takes A, B and C, and who submits on the portal.

Daily rhythm:

- 10:00 AM IST: a 15-minute call to cover yesterday, today and blockers.
- 10:00 PM IST: each person moves their tasks' status and writes one line on blockers.
- A blocker older than 4 hours goes to the whole team, not just the owner.

Timeline

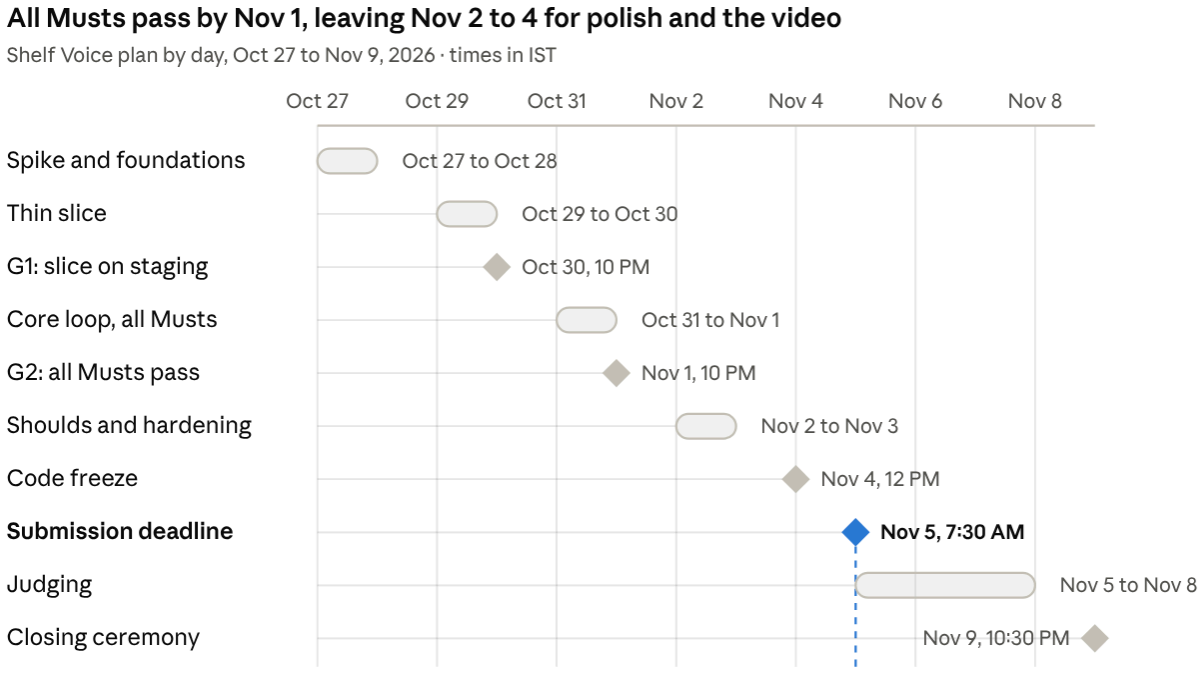

build plan by day · 5 phases, 2 gates, freeze and deadline

G1 and G2 are the two checkpoints. If G2 slips, Nov 2 goes to fixing Musts before any Should (I3), and the noon freeze still leaves about 19 hours before the deadline.

Day-1 spike

The spike proves the four unknowns behind the whole plan by Oct 28, 9 PM IST, before anyone builds on them. Each check gets PASS, FAIL or BLOCKED, with evidence saved under `spike/` in the repo: request, response, and the recorded audio or photo.

#	Check	PASS means	If it fails
S0	Claim the $150 credit and create the API key	Key works in the Meta dashboard; the credit's exact end date is recorded (K4); stored only in Vercel and the shared vault (R6)	BLOCKED: ask organisers in the hackathon channel on day 1
S1	Meta API reachable from India	muse-spark-1.3 Responses call returns 200 from a laptop in India and from a Vercel function in bom1	Route calls through the fallback provider named in document 02; note it in the README

#	Check	PASS means	If it fails
S2	Structured output	10 sample owner transcripts return JSON that passes our Zod schemas through `text.format`	Add one repair retry, then fall back to tool calling
S3	Transcribe request and response shape	Exact multipart field names, `keywords`, `languageBias` and `mode` confirmed; one response saved as a test fixture	Read the API reference and ask in the channel; Must items stay on track with typed input until it works
S4	Hinglish accuracy	20 clips (10 owner commands, 10 reviews) from all 3 teammates meet the document 04 thresholds for product names and quantities	Feed the catalog into `keywords`, and keep every number editable on the confirm screen
S5	SAM 3.1 masks	One shelf photo returns masks we can decode and crop into a product image	FR-10 is dropped; Musts are not affected
S6	Region latency	Vercel bom1 to Supabase ap-south-1 query under 50 ms at p95 over 100 calls	Check regions in both dashboards before going further

Go or no-go at 9 PM IST on Oct 28: S0 to S3 must be PASS or have a working fallback, or the team spends Oct 29 morning on them before starting the thin slice. S4 and S5 only change scope, never the start.

Work breakdown

Every task has one owner, maps to a requirement where it can, and is done only when its check passes. Status moves from Not started to Complete; Blocked always has a one-line reason in the tracker (I6).

ID	Task	FR	Owner	Done when	Status
P0 Spike and foundations, Oct 27 to 28					

ID	Task	FR	Owner	Done when	Status
W-01	Repo, Next.js strict TypeScript, pnpm, lint, CI skeleton	—	B	CI green on an empty app	Not started
W-02	Supabase staging and production, document 07 migrations, RLS, pgTAP tests	—	B	`supabase test db` PASS on staging	Not started
W-03	Vercel project in bom1, env vars, Axiom, Better Stack, keep-alive	—	B	Preview and production URLs load; logs reach Axiom	Not started
W-04	Meta API client: Responses, transcribe, SAM; Zod; `ai_calls` logging; spend breaker	—	C	Unit tests PASS with recorded responses	Not started
W-05	Day-1 spike S0 to S6	—	C	All seven checks have a status and evidence	Not started
W-06	Design tokens, shadcn theme, app shell with four tabs and mic	—	A	Shell matches the mockups at 390 px	Not started
P1 Thin slice, Oct 29 to 30					
W-07	Google sign-in and "Try the demo shop"	FR-01	B	Sign-in works; demo copy expires after 24 h	Not started
W-08	Mic capture, WAV encode, signed upload to Storage	FR-02	A	A 60 s clip uploads from a mid-range Android	Not started
W-09	Voice setup extraction and confirm screen	FR-02, FR-03	C, A	Spoken setup becomes a confirmed shop and catalog	Not started
W-10	Public storefront, QR code, WhatsApp ordering	FR-04	A	Storefront loads in under 2.5 s LCP on 4G	Not started
P2 Core loop, Oct 31 to Nov 1					
W-11	Voice catalog edits	FR-05	C	Edit evals meet document 04 thresholds	Not started

ID	Task	FR	Owner	Done when	Status
W-12	Voice sales and stock logging	FR-06	B	Movements logged; `stock_qty` matches the trigger	Not started
W-13	Forecast and order list	FR-07	B	Forecast unit tests PASS on the document 07 cases	Not started
W-14	Customer voice review: consent, Turnstile, 15 s limit	FR-08	A	Review saved with no account; rate limits hold	Not started
W-15	Review insight and restock priority	FR-09	C	Stock-out mentions raise the item in the order list	Not started
W-16	Supplier bill photo to stock	FR-11	C	Bill lines become a proposal the owner confirms	Not started
W-17	Self-serve delete shop	FR-16	B	Shop, data and files gone within 24 h	Not started
P3 Shoulds and hardening, Nov 2 to 3					
W-18	Shelf photo with SAM 3.1 (only after the Nov 1 gate)	FR-10	C	Cut-outs appear as storefront images	Not started
W-19	Festival bump	FR-12	B	Forecast rises before a calendar festival	Not started
W-20	Daily summary card	FR-13	A	Today shows sales, low stock and new reviews	Not started
W-21	Seeded demo shop with 90 days of sales	—	B	Order list shows believable numbers on camera	Not started
W-22	Evals, security checks, Lighthouse, k6	—	C	Release checklist rows PASS	Not started
W-23	Real-owner sessions (I4)	—	A	Signed consent and recordings saved	Not started
P4 Freeze and submit, Nov 4					
W-24	Release from document 08 checklist; freeze at noon IST	—	B	Checklist complete on the release commit	Not started

ID	Task	FR	Owner	Done when	Status
W-25	Demo video, 2 to 3 minutes	—	A	Video uploaded; plays without sign-in	Not started
W-26	Submit on the Cerebral Valley portal	—	Submitter	Confirmation email received	Not started

Gate G1, Oct 30 at 10 PM IST: a new owner can speak, confirm and see a live storefront on staging.

Gate G2, Nov 1 at 10 PM IST: every Must passes on staging. FR-14 and FR-15 (Could) are not planned.

Status rules and definition of done

Task status and check results use separate words, so "Complete" always rests on evidence.

Word	Applies to	Means
Not started, In progress, Blocked, Complete	Tasks (W-01 to W-26)	Where the work stands; Blocked carries a reason and the person who can unblock it
PASS, FAIL, BLOCKED, NOT RUN, NOT APPLICABLE	Checks (spike, release checklist, acceptance tests)	The result of one check, with a link to its evidence

A task is Complete only when all of these are true:

1. Its "Done when" check is PASS, with the evidence linked in the PR: a CI run, test output, a screenshot or a recording.
2. The code is merged to main through a reviewed PR, and CI is green on that commit.
3. It runs on staging, or on production after G2.
4. Every new user-visible string exists in Hindi and English.
5. Any new table has RLS and a pgTAP test, and any new model call is logged in `ai_calls` with a spend cap.
6. No secret appears in the repo, logs or PR text.

Nobody reports a check as PASS without its evidence. A check that was not run is NOT RUN, not assumed.

Risks and blockers

The biggest risk is the Meta API path from India, so the spike tests it first. No blockers are recorded yet; a blocker is a risk that has already happened, and it is logged in the tracker with its owner.

#	Risk	Likelihood	Impact	Mitigation	Watched by
K1	Meta API key, credits or region access delayed	Medium	High	Spike S0 and S1 on day 1; fallback route from document 02	C
K2	Hinglish transcription misreads product names or quantities	Medium	High	Catalog `keywords`; every number editable on confirm; eval suite on 20+ clips	C
K3	Credit runs out before judging ends	Low	High	Daily caps, AI breaker, alerts at 50% and 80% of the credit; recorded responses in CI	C
K4	The $150 credit is valid for a 10-day window that may end before the Nov 9 final	Medium	High	S0 records the exact end date; if it falls before Nov 9, the demo shop replays saved AI results so judges never hit a dead API	C
K5	Scope grows past the time	High	High	G2 gate on Nov 1; Shoulds only after it (I3)	All
K6	A teammate becomes unavailable	Medium	Medium	Each area has a named backup and the runbook (document 08)	All
K7	Real shop owners not reachable by Nov 3	Medium	Medium	Line up owners by Oct 31; if none, say so honestly and demo the seeded shop	A
K8	Live demo breaks during judging	Low	High	Seeded demo shop, uptime alerts, on-call rotation, recorded video as backup	B
K9	Portal asks for something we did not plan (format, length, repo rules)	Medium	Medium	Read the submission form on Oct 28 and again on Nov 2	Submitter
K10	Freeze at noon Nov 4 squeezes video time	Medium	Medium	Script and shot list ready by Nov 3; recording starts 1 PM IST Nov 4	A
K11	Supabase free project pauses or hits a limit	Low	Medium	Keep-alive check; usage watched daily (document 08)	B

Submission and demo video

The submission goes in by Nov 4, 11 PM IST (I5), and the form is read on Oct 28 so nothing in it is a surprise. The organisers had not published the full form as of Oct 17, so this list grows when we read it.

- [ ] Read the Cerebral Valley submission form and copy its fields here (Oct 28)
- [ ] Indie track selected; all 3 teammates listed
- [ ] Live link to the free Vercel subdomain (R5), with "Try the demo shop" working without sign-in
- [ ] Public GitHub repo; README covers the problem, setup, architecture, the Meta models used and how numbers are computed
- [ ] Demo video, 2 to 3 minutes, recorded from the release commit and playable without sign-in
- [ ] Problem statements named, and how Shelf Voice covers all three
- [ ] No secrets, private data or customer recordings without consent in the repo or video
- [ ] Confirmation received and saved in the shared vault

Video plan, written by Nov 3 and recorded from 1 PM IST on Nov 4. Each beat leads with the judging criterion it serves:

Beat	Shows	Criterion
Opening	A real kirana owner, the problem in one line, and the three gaps: no online shop, guessing reorders, no customer feedback	Impact (30%)
Voice to storefront	Owner speaks in Hinglish; transcript and changes appear on confirm; one tap publishes the storefront	Meta tooling (25%)
Customer review	Customer scans the QR and records 15 seconds; "atta khatam tha" raises Atta on the order list	Meta tooling, Technical depth (20%)
Order list	Days left and order quantity, with why the numbers come from code and not the model	Technical depth
Real owners	Two or three short quotes from the I4 sessions	Impact
Close	Live link, repo, the three Meta models used	Demo (25%)

Judging week and after

From Nov 5, 7:30 AM IST, the job is to keep the submitted build working exactly as judged until the Nov 9, 10:30 PM IST closing ceremony.

- On-call in 8-hour shifts across 24 hours, as set in documents 05 and 08.
- Only security fixes are merged, through manual promotion with a rollback ready.
- Each morning, the on-call person opens the live link and runs "Try the demo shop". They also check credit left against its end date (K4) and the uptime monitors.
- If we reach the top 10, prepare a live final run on Nov 8 and 9: a scripted 3-minute walk-through, a backup recording, and two phones charged and signed in.
- After Nov 9, decide in one call whether to keep the shop running, archive it, or delete stored customer audio early. The 30-day deletion runs either way.

Sources

Checked Oct 27, 2026.

- Official hackathon rules, shared by the owner: judging criteria (Impact 30%, Meta tooling 25%, Technical depth 20%, Demo 25%), one track per team, and $150 in credits "valid for a 10-day development window"
- Cerebral Valley event page: dates Oct 26 to Nov 4, 9 PM ET; submissions due Nov 5 UTC
- Hackathon timeline repo: judging Nov 5 to 8, closing ceremony Nov 9 at 12 PM, last day to claim credits Nov 4
- Shelf Voice documents 01 to 08 in this project, for requirement IDs, thresholds and operating rules
